



City of Redlands: Municipal Utilities & Engineering Department
35 Cajon Street, Suite 15A, Redland, CA 92373
(909) 798-7698

2023 CIP SEWER PIPELINE REPLACEMENT PROJECT


City Engineer: Goutam Dobey
Phone: (909) 435-7431 (Cell)
Email: gdobey@cityofredlands.org

City Inspector: Chris Mergener
Phone: (909)253-8698 (Cell)
Email: cmergener@cityofredlands.org

PROJECT DETAILS

Contractor: ALL CITIES ENGINEERING, INC.
Description: This project will involve rehabilitating approximately 18,000 linear feet of sewer pipeline and the removal and replacement of various manholes.
Start Date: 07/18/2024
Anticipated End Date: November 2024
Work Schedule: M-F (7AM - 4PM) excluding city recognized holidays.

CONSTRUCTION PROGRESS

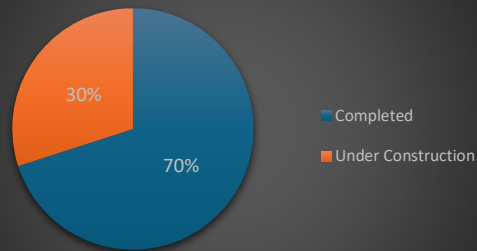

Project Updates & Issues

The lead time for materials required for the Cured-In-Place Pipe (CIPP) installation is causing a delay in the start date for the work.

2-Week Look Ahead

The construction crew will continue restriping all newly paved trench lines. The crew will rehabilitate the pipeline using Cured-In-Place Pipe (CIPP) for all sections marked in red on the map.

Current Construction Process

Construction notices have been given to affected residents. If restricted parking is necessary, "No Parking" signs will be posted 48 hours in advance of construction activities.



Night work replacing sewer line on Cajon Street and State Street

BUDGET TRACKING


Project Cost:	\$	2,485,353.00
Approved Change Orders	\$	-
Total Contract Value	\$	2,485,353.00
Expended to Date:	\$	1,628,940.00
Balance:	\$	856,413.00

ADDITIONAL INFORMATION

Register online to receive weekly updates by sending an email with the subject line: 2023 CIP Sewer Project Updates. To: MUEDProjectUpdate@cityofredlands.org

INTERACTIVE CITY CAPITAL IMPROVEMENT PROJECT MAP LINK:

<https://www.cityofredlands.org/node/3710>

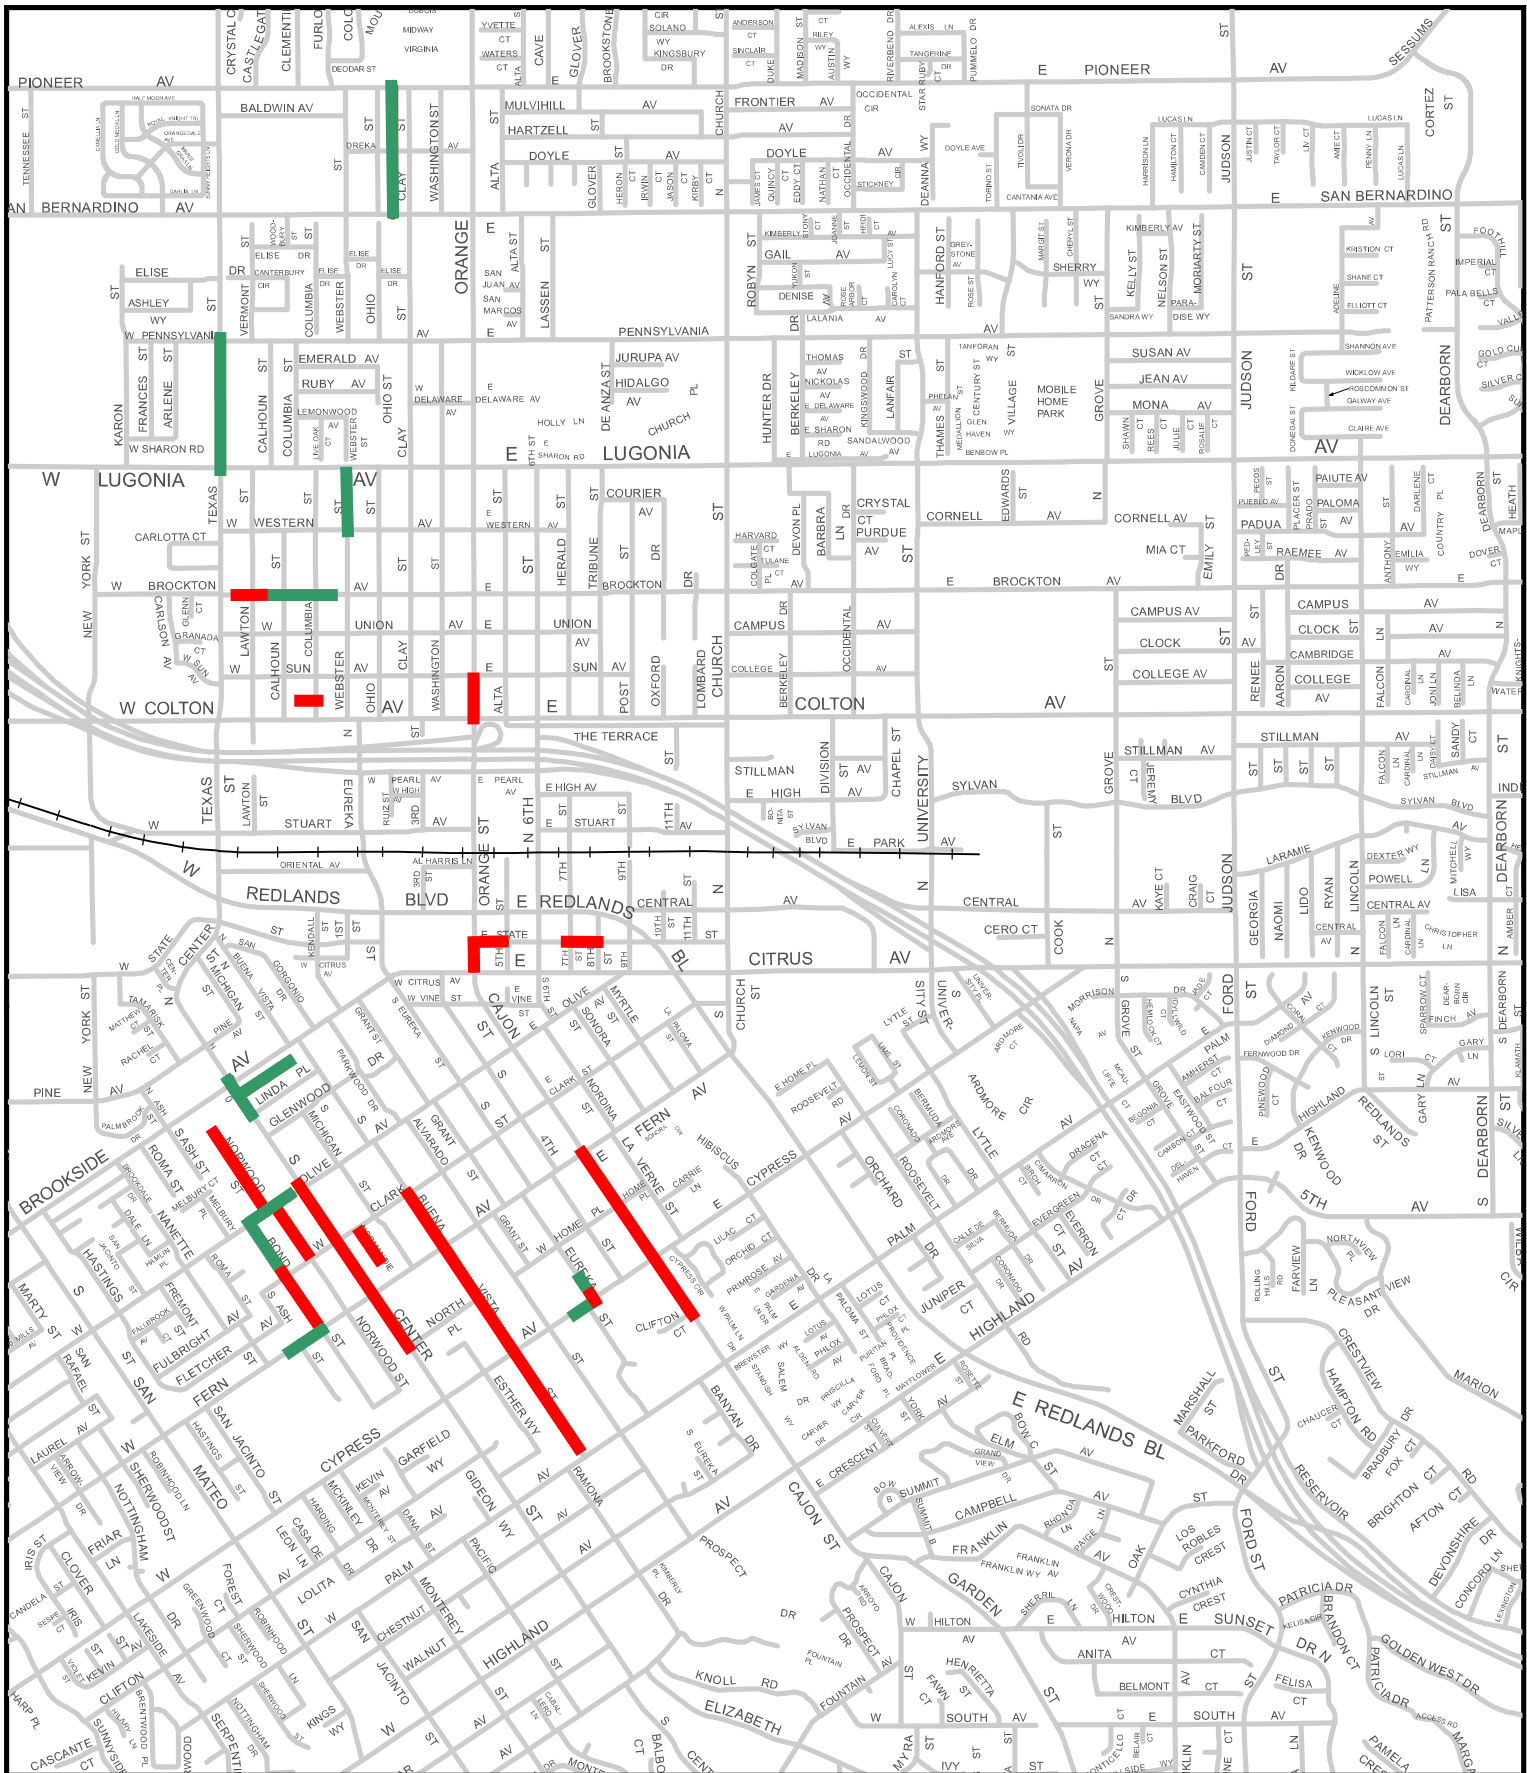

2023 CIP SEWER PIPELINE REPLACEMENT PROJECT LOCATION MAP

- Completed
- Under Construction

