



City of Redlands: Municipal Utilities & Engineering Department
35 Cajon Street, Suite 15A, Redland, CA 92373
(909) 798-7698

2023 CIP SEWER PIPELINE REPLACEMENT PROJECT


City Engineer: Goutam Dobey
Phone: (909) 435-7431 (Cell)
Email: gdobey@cityofredlands.org

City Inspector: Chris Mergener
Phone: (909)253-8698 (Cell)
Email: cmergener@cityofredlands.org

PROJECT DETAILS

Contractor: ALL CITIES ENGINEERING, INC.
Description: This project will involve rehabilitating approximately 18,000 linear feet of sewer pipeline and the removal and replacement of various manholes.
Start Date: 07/18/2024
Anticipated End Date: November 2024
Work Schedule: M-F (7AM - 4PM) excluding city recognized holidays.

CONSTRUCTION PROGRESS

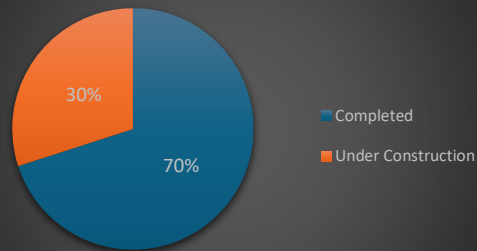

Project Updates & Issues

Striping and pavement markings are being installed on streets that have had sewer lines recently replaced. The lead time for materials required for the Cured-In-Place Pipe (CIPP) installation is causing a delay in work.

2-Week Look Ahead

CIPP installation is currently on hold due to delays in material lead times.

Current Construction Process

Construction notices have been given to affected residents. If restricted parking is necessary, "No Parking" signs will be posted 48 hours in advance of construction activities.



Manhole installation on Bond Street

BUDGET TRACKING


<i>Project Cost:</i>	\$	2,485,353.00
<i>Approved Change Orders</i>	\$	-
<i>Total Contract Value</i>	\$	2,485,353.00
<i>Expended to Date:</i>	\$	1,875,340.00
<i>Balance:</i>	\$	610,013.00

ADDITIONAL INFORMATION

Register online to receive weekly updates by sending an email with the subject line: 2023 CIP Sewer Project Updates. To: MUEDProjectUpdate@cityofredlands.org

INTERACTIVE CITY CAPITAL IMPROVEMENT PROJECT MAP LINK:

<https://www.cityofredlands.org/node/3710>

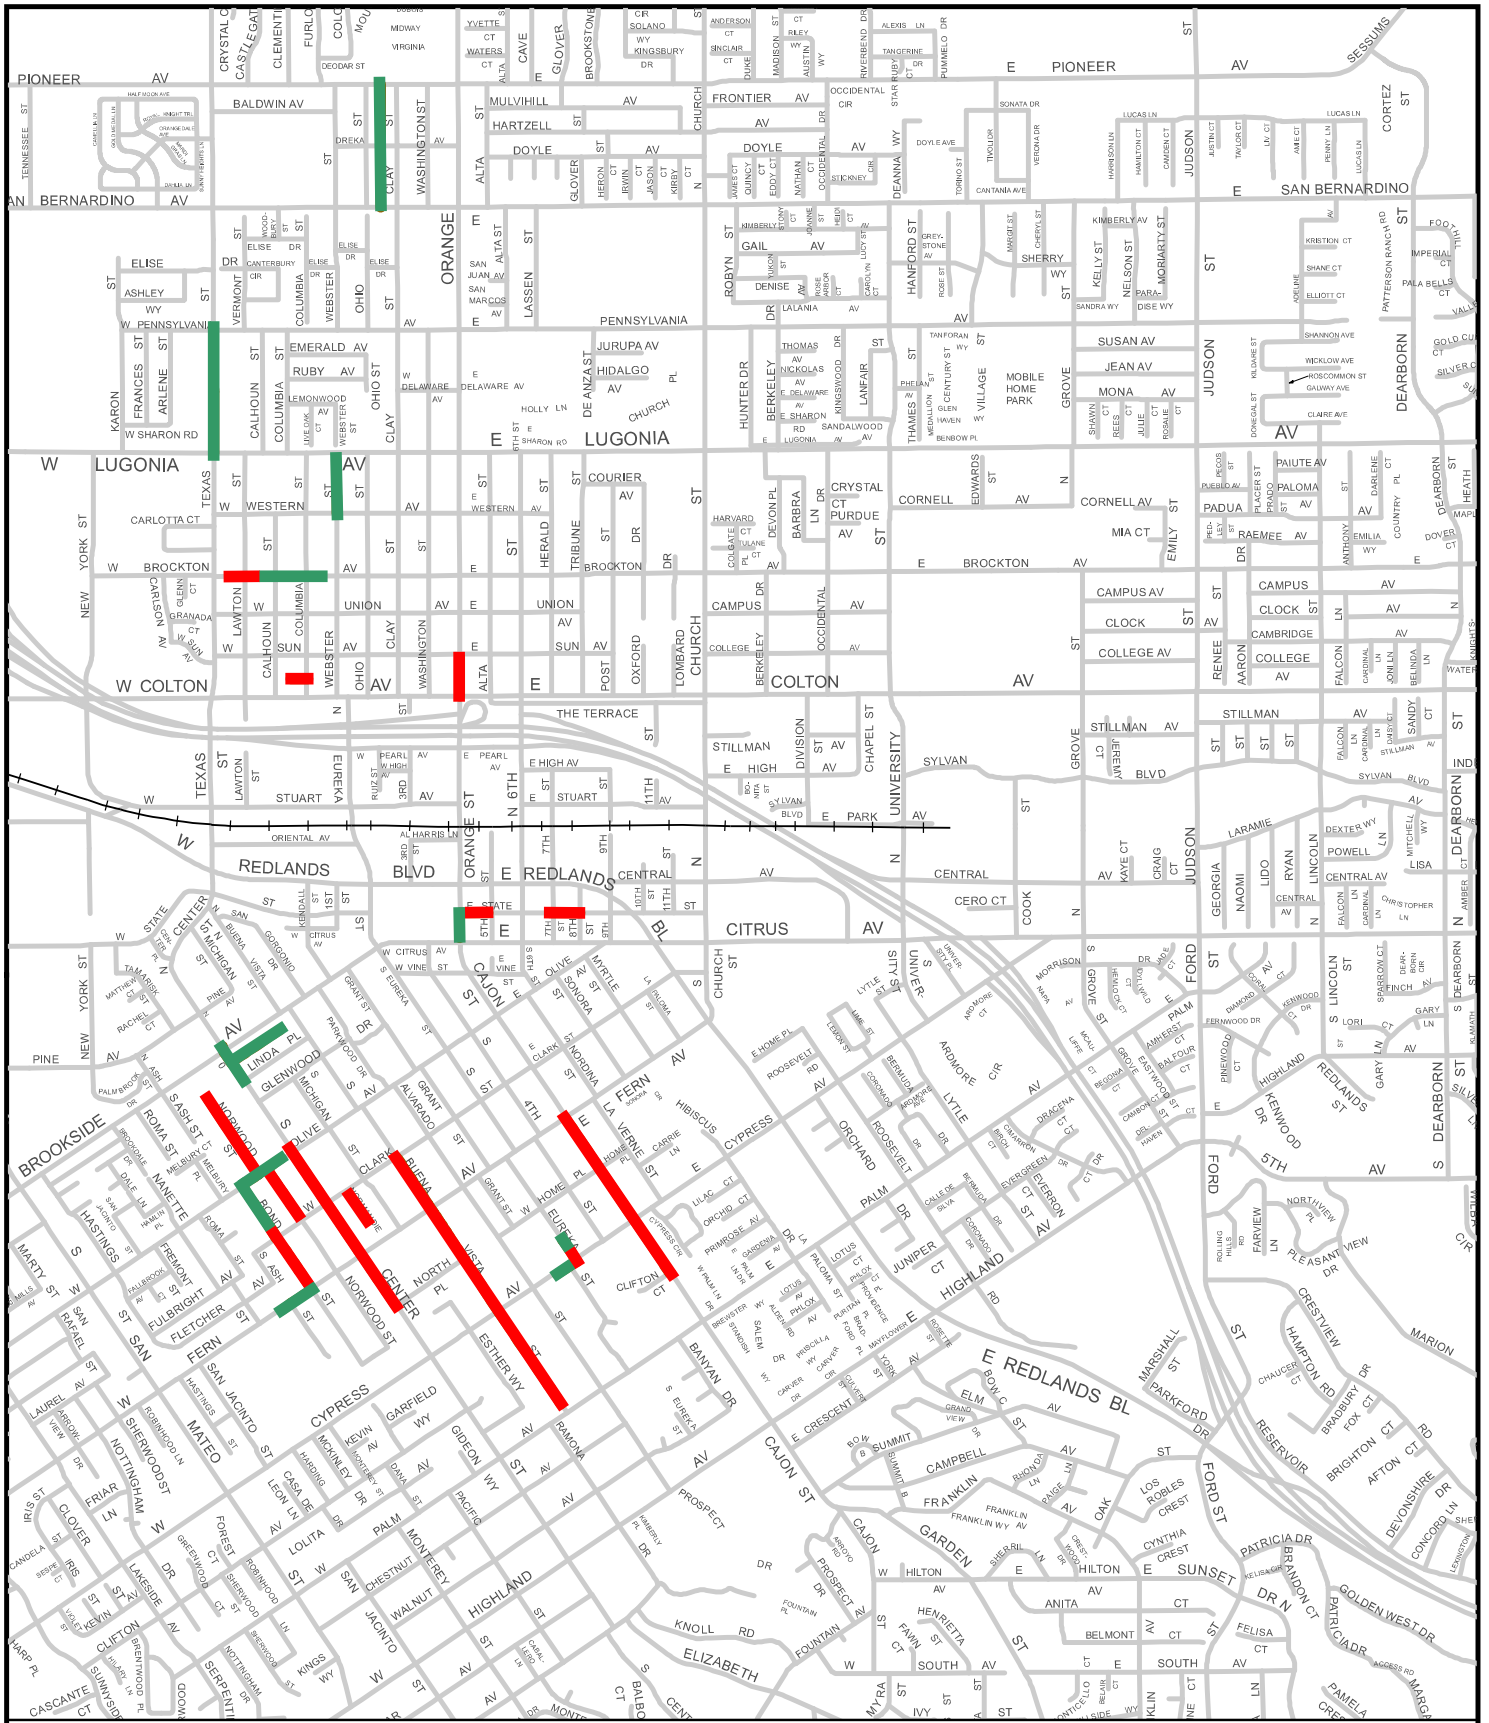

2023 CIP SEWER PIPELINE REPLACEMENT PROJECT LOCATION MAP

- Completed
- Under Construction

