



City of Redlands: Municipal Utilities & Engineering Department
 35 Cajon Street, Suite 15A, Redlands, CA 92373
 (909) 798-7698

PMP 2024 STREET RESURFACING PROJECT


City Engineer: Goutam Dobey
 Phone: (909) 435-7431 (Cell)
 Email: gdobey@cityofredlands.org

City Inspector: Daniel Murbarger
 Phone: (909) 437-8440 (Cell)
 Email: dmurbarger@cityofredlands.org

PROJECT DETAILS

Contractor: Matich Corporation
Description: This project will replace approximately twenty-eight (28) lane miles of streets, selective replacement of curb and gutter, and striping replacement at various locations throughout the City.
Start Date: 10/15/2024
Anticipated End Date: February 2025
Work Schedule: M-F (7am - 4PM) excluding city recognized holidays.

CONSTRUCTION PROGRESS

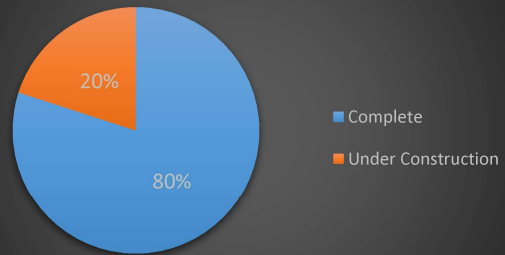

Project Updates & Issues


The Contractor has completed paving Greenspot Road, Garnet Street, and Amethyst Street. The raising of manholes, installation of traffic loops, and installation of striping and pavement markings on recently paved streets will be complete by the end of week.

2 Week Look Ahead

There will be no major work associated with this project from next week until the New Year. Beginning January 7, 2025, full depth reclamation work will proceed on Live Oak Canyon Road.

Current Construction Process

Construction notices have been given to affected residents. If restricted parking is necessary, "No Parking" signs will be posted 48 hours in advance of construction activities. Please take the proper precautions, and follow posted construction signs and installed traffic control.

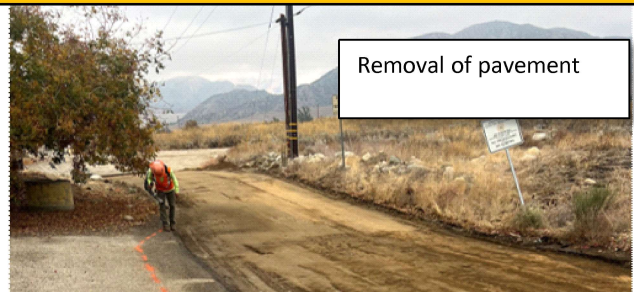

BUDGET TRACKING


Project Cost:	\$	4,677,377.00
Approved Change Orders	\$	-
Total Contract Value	\$	4,677,377.00
Expended to Date:	\$	1,025,803.25
Balance:	\$	3,651,573.75

ADDITIONAL INFORMATION

Register for the distribution list to receive regular updates by sending an email to:
MUEDProjectUpdate@cityofredlands.org

CITY CAPITAL IMPROVEMENT PROJECT MAP LINK:

<https://www.cityofredlands.org/node/3710>

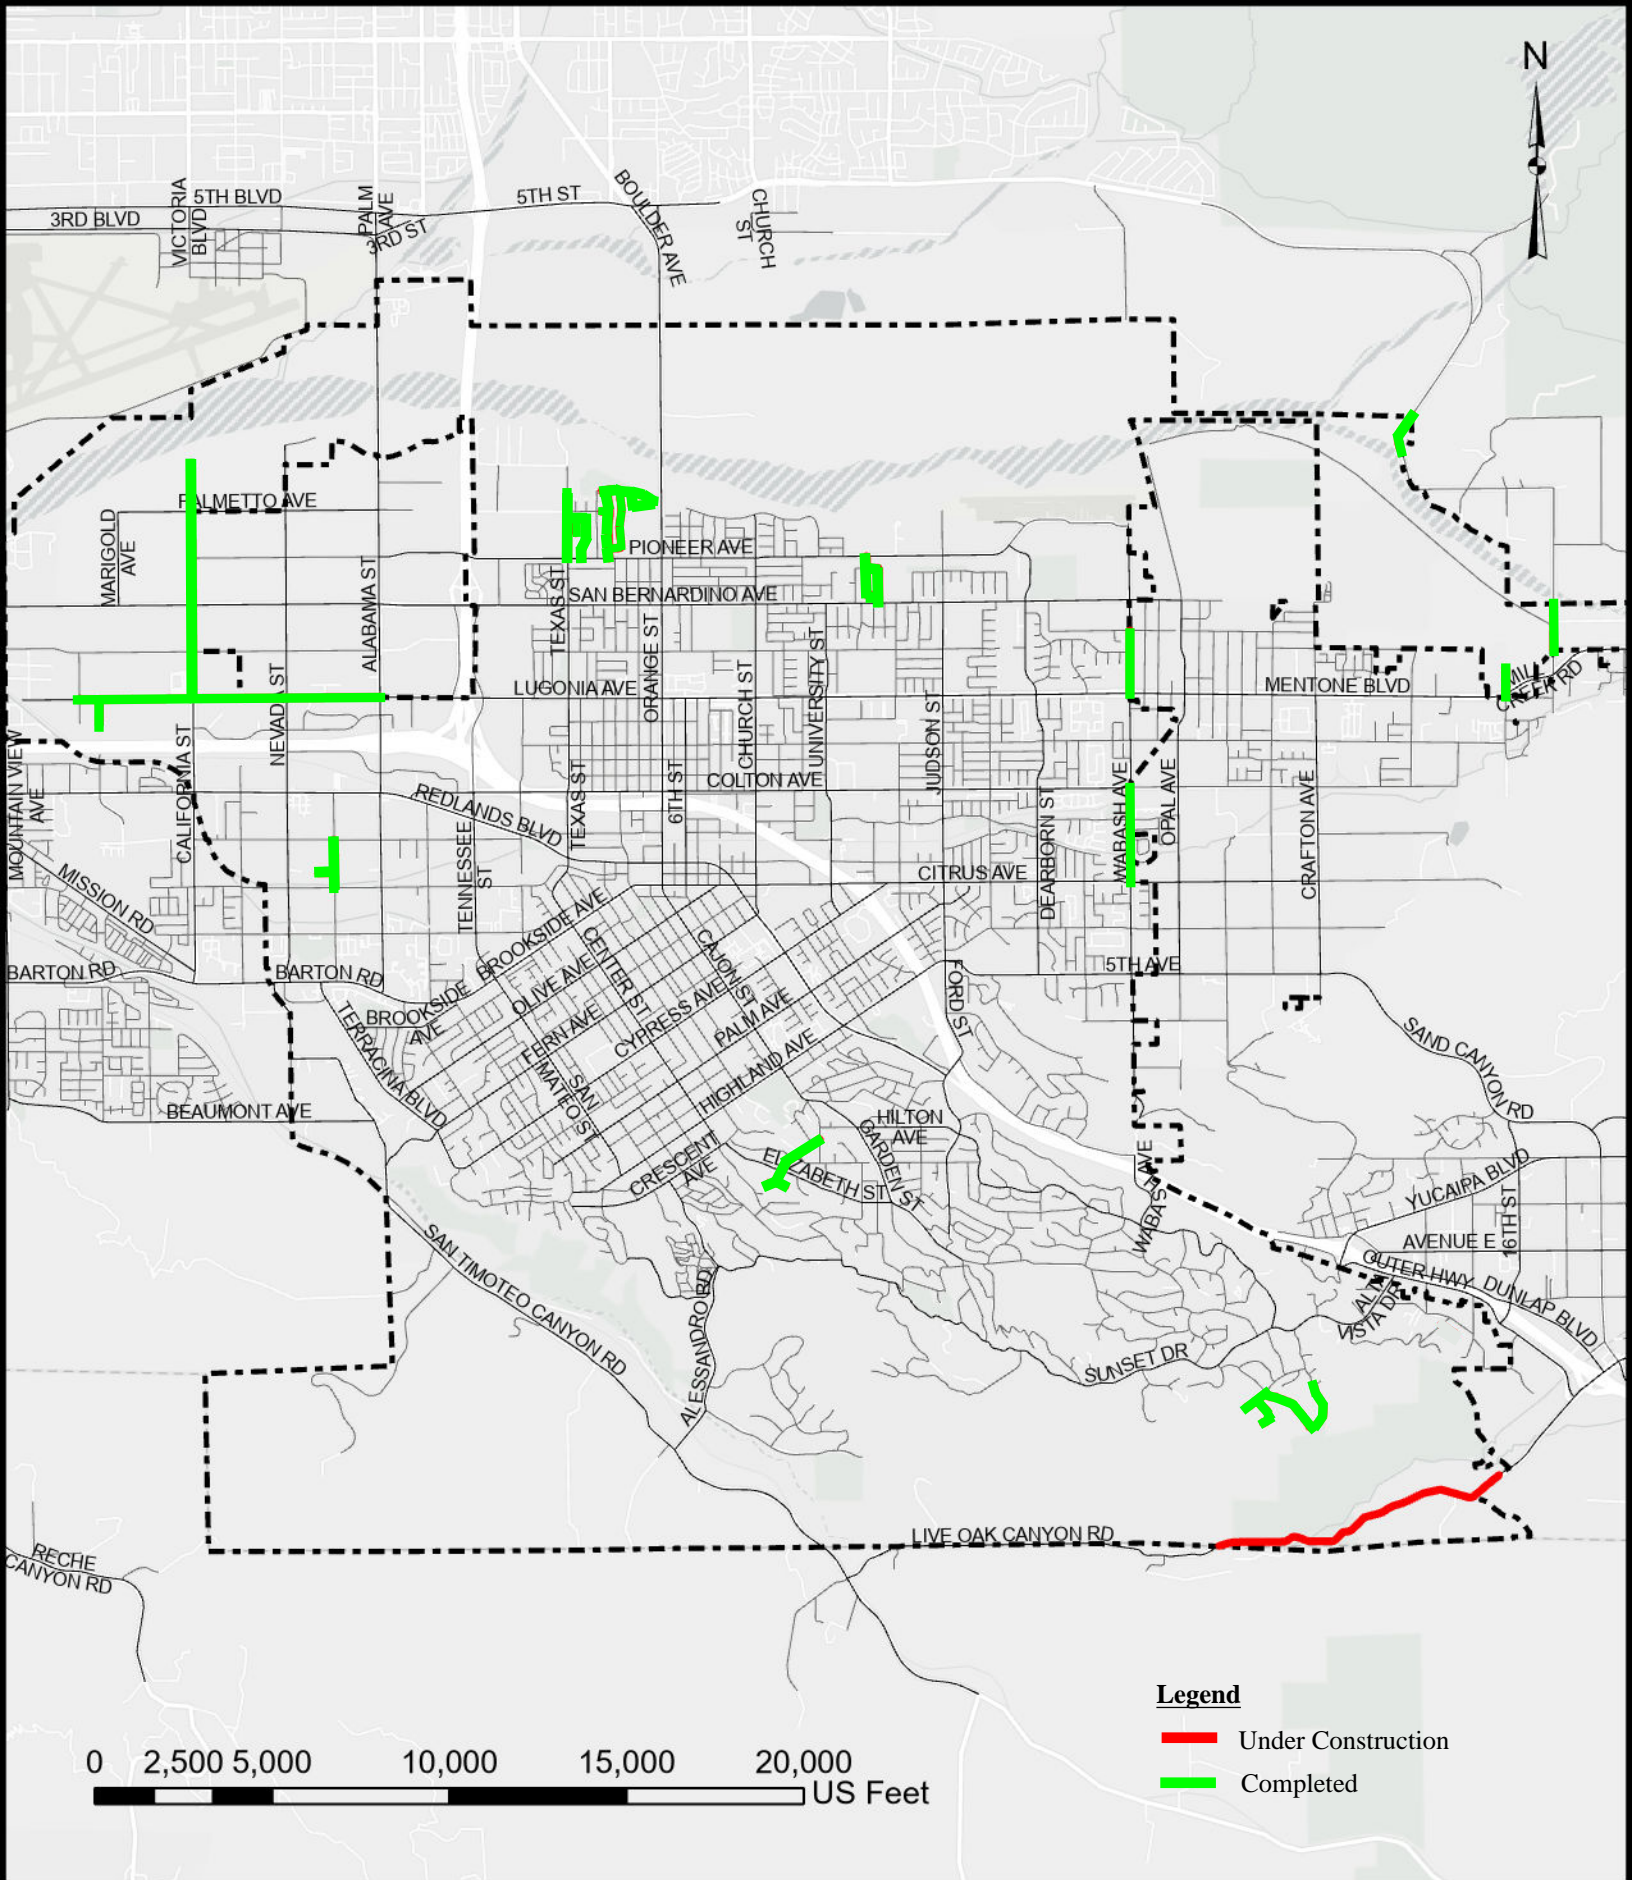

Legend

- Under Construction
- Completed



City of Redlands
PMP 2024 STREET RESURFACING PROJECT
LOCATION MAP
